




# Monthly Progress Report

June 2022

Lindenhurst Memorial Library



1 Lee Avenue, Lindenhurst, N.Y. 11757



# Table of Contents

**Section I – Work Progress** June 2022

**Section II – Work Projected for** July 2022

**Section III – Progress Photos**

**Section IV – Monthly Workforce Summary**



## Section I - Work Progress

June 2022

- Finished welding structural steel at new addition
- Installed metal decking and poured slab on new addition mezz
- Finished framing and started sheathing of exterior of new addition and North soffit
- Installed roof over new addition
- Started brickwork around outside of new addition
- Finished framing and installing glass in North window bumpouts
- Installed flooring on mezzanine and protected
- Installed storefront in quiet study
- Finishing taping of all walls in renovation portion of building
- Installed storefront in basement courtyard
- Finished ceiling throughout basement
- Poured ramp and infilled slab in courtyard
- Started install of linear lights throughout site



## Section II - Work Planned

July 2022

- Pour curbs and sidewalks throughout site
- Rough grade parking lot
- Begin EIFS install around on North Soffit and new addition
- Finish exterior masonry around new addition
- Frame interior walls in new addition
- Rough-in MEP's in new addition
- Begin sheetrock inside new addition
- Begin install of wood ceiling throughout
- Whiteout all ACT ceilings
- Install flooring throughout basement and first floor
- Begin delivery and set up of casework in phase 1



Section III – Progress Photos



New addition mezz slab poured and roof flashed-in





## Section III – Progress Photos



Interior and exterior of new addition



## Section III – Progress Photos



Exterior brick at new addition and North window bumpouts





## Section III – Progress Photos



Mezz flooring installed (top) and quiet study storefront installed (bottom)





## Section III – Progress Photos




Basement courtyard Nanawall and storefront installed



## Section IV – Workforce Summary – Company/Hours

June 2022

### MANPOWER GRAPH

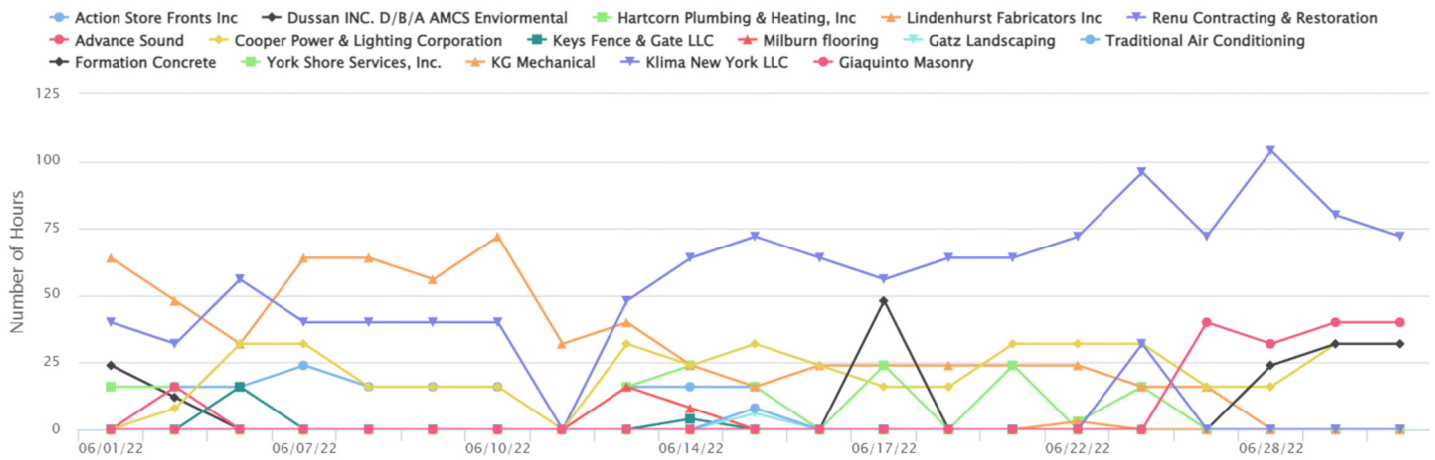



Lindenhurst Memorial Library

June 2022

# End of Progress Report
